Montana Public Safety Communications System

SIGB
By
Warren Dupuis
September 11, 2012

Purpose

- Provide an update the Montana Public Safety Communications System Project

Current Program Overview

Progress Made to Original Plan

Infrastructure				Microwave				Trunking			
Complete	In progress	Planned	Total	Complete	In progress	Planned	Total	Complete	In progress	Planned	Total
96	**4**	**39**	**139**	**86**	**6**	**45**	**137**	**48**	**6**	**64**	**118**
69%	**3%**	**28%**		**63%**	**4%**	**33%**		**41%**	**5%**	**54%**	

PUBLIC SAFETY COMMUNICATIONS SYSTEM

Trunk Status 5/4/2012

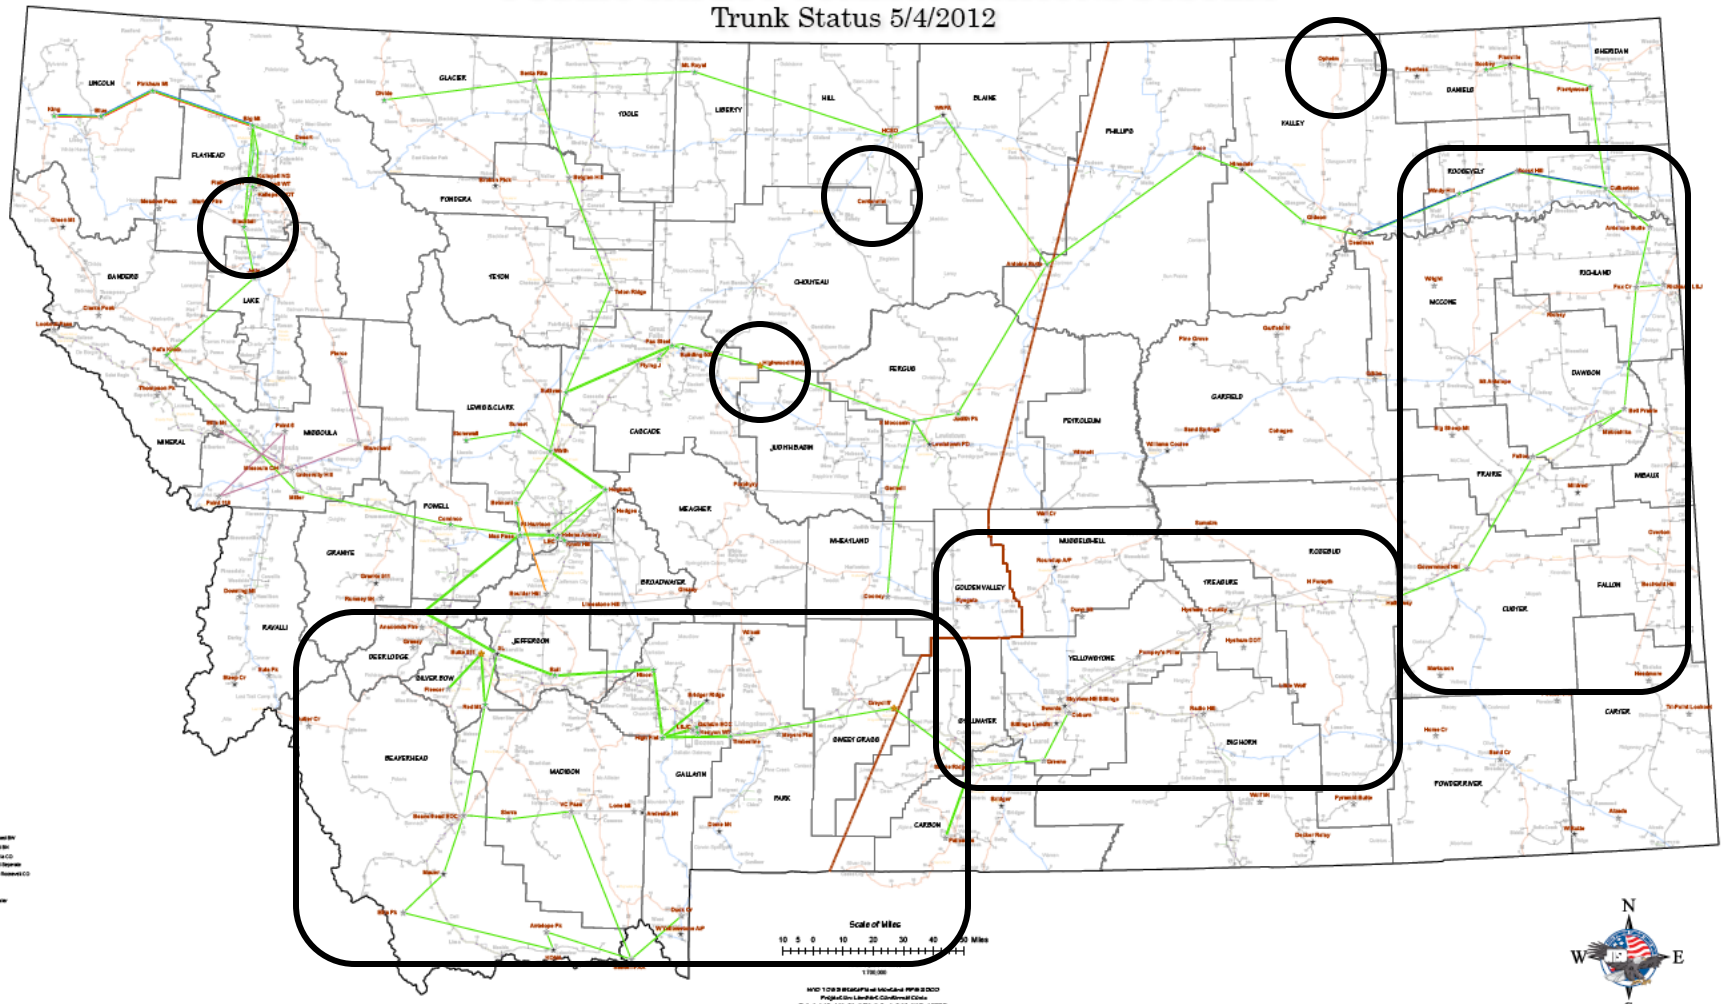

North East Microwave & Trunking

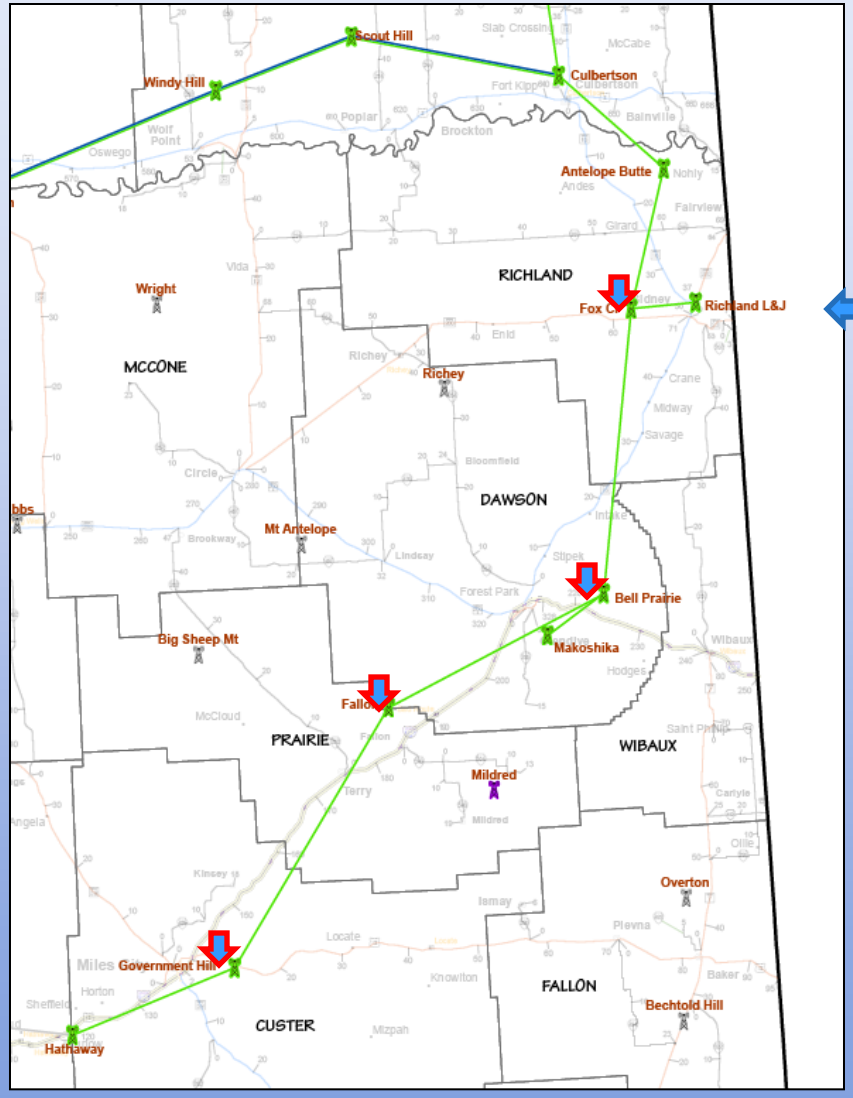

2nd Zone Controller

South West Trunking

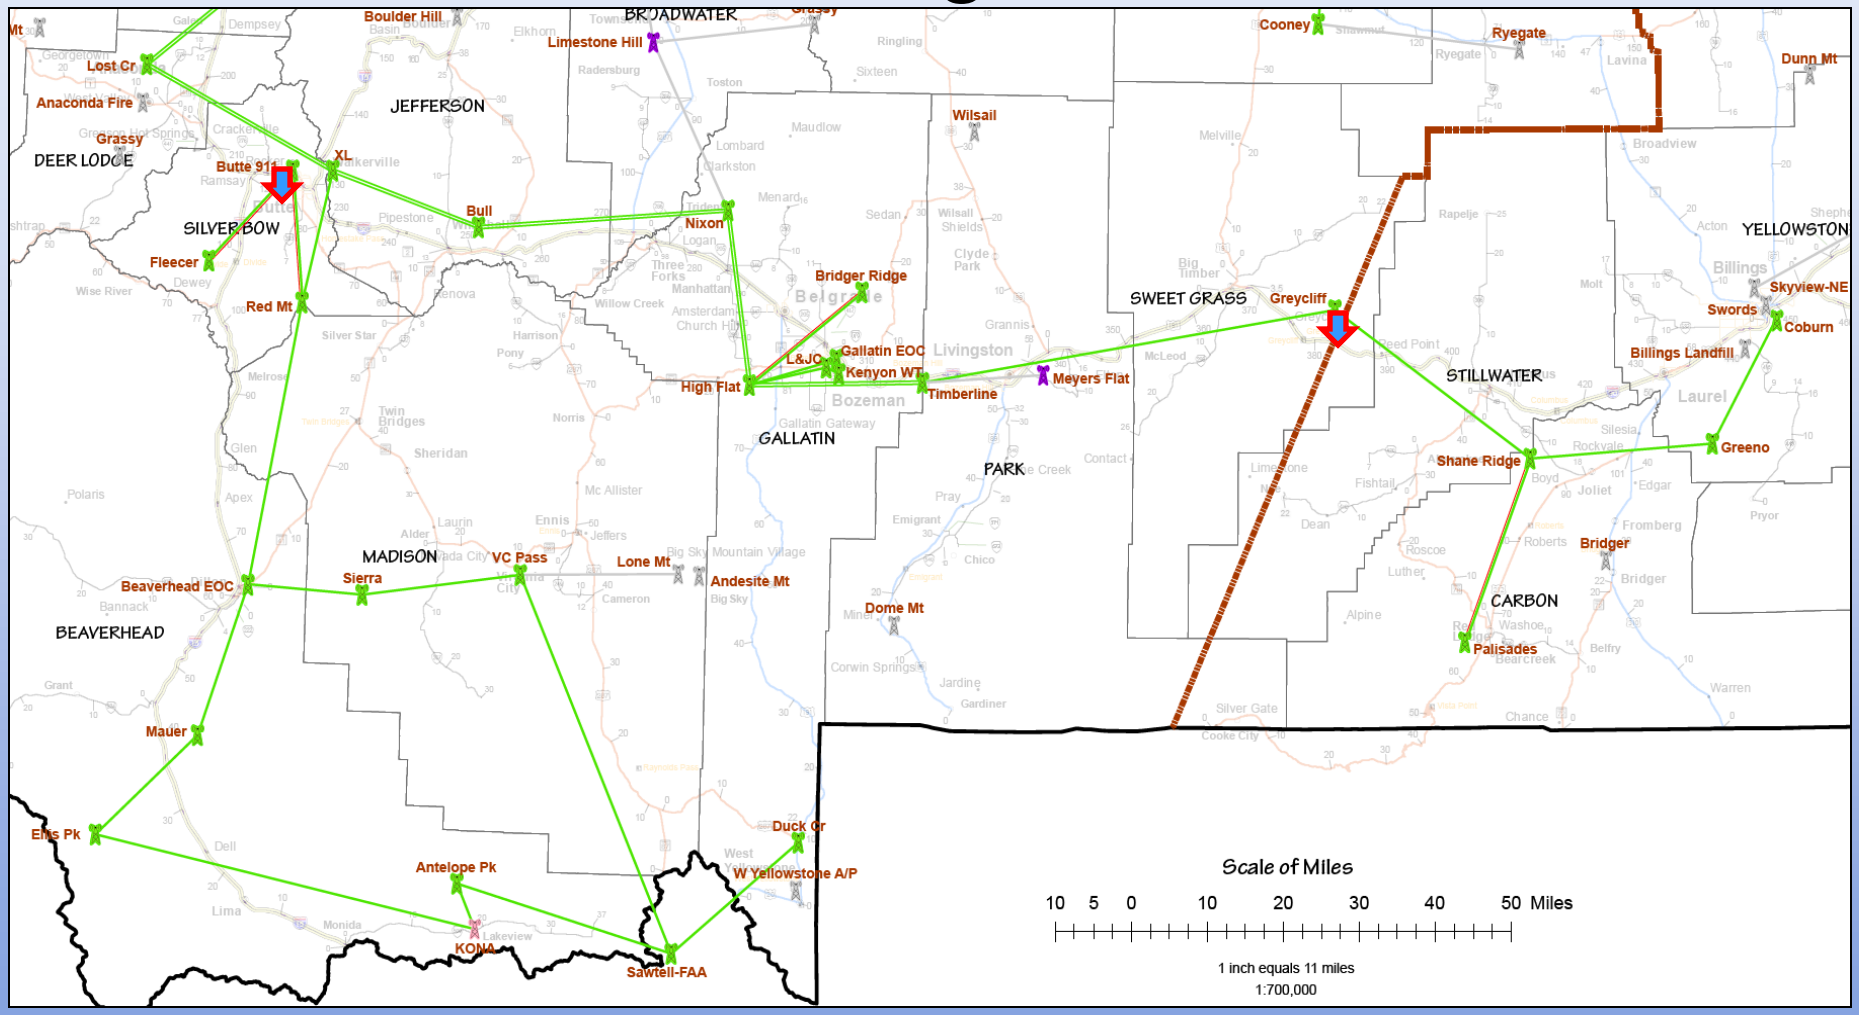

South Central Microwave

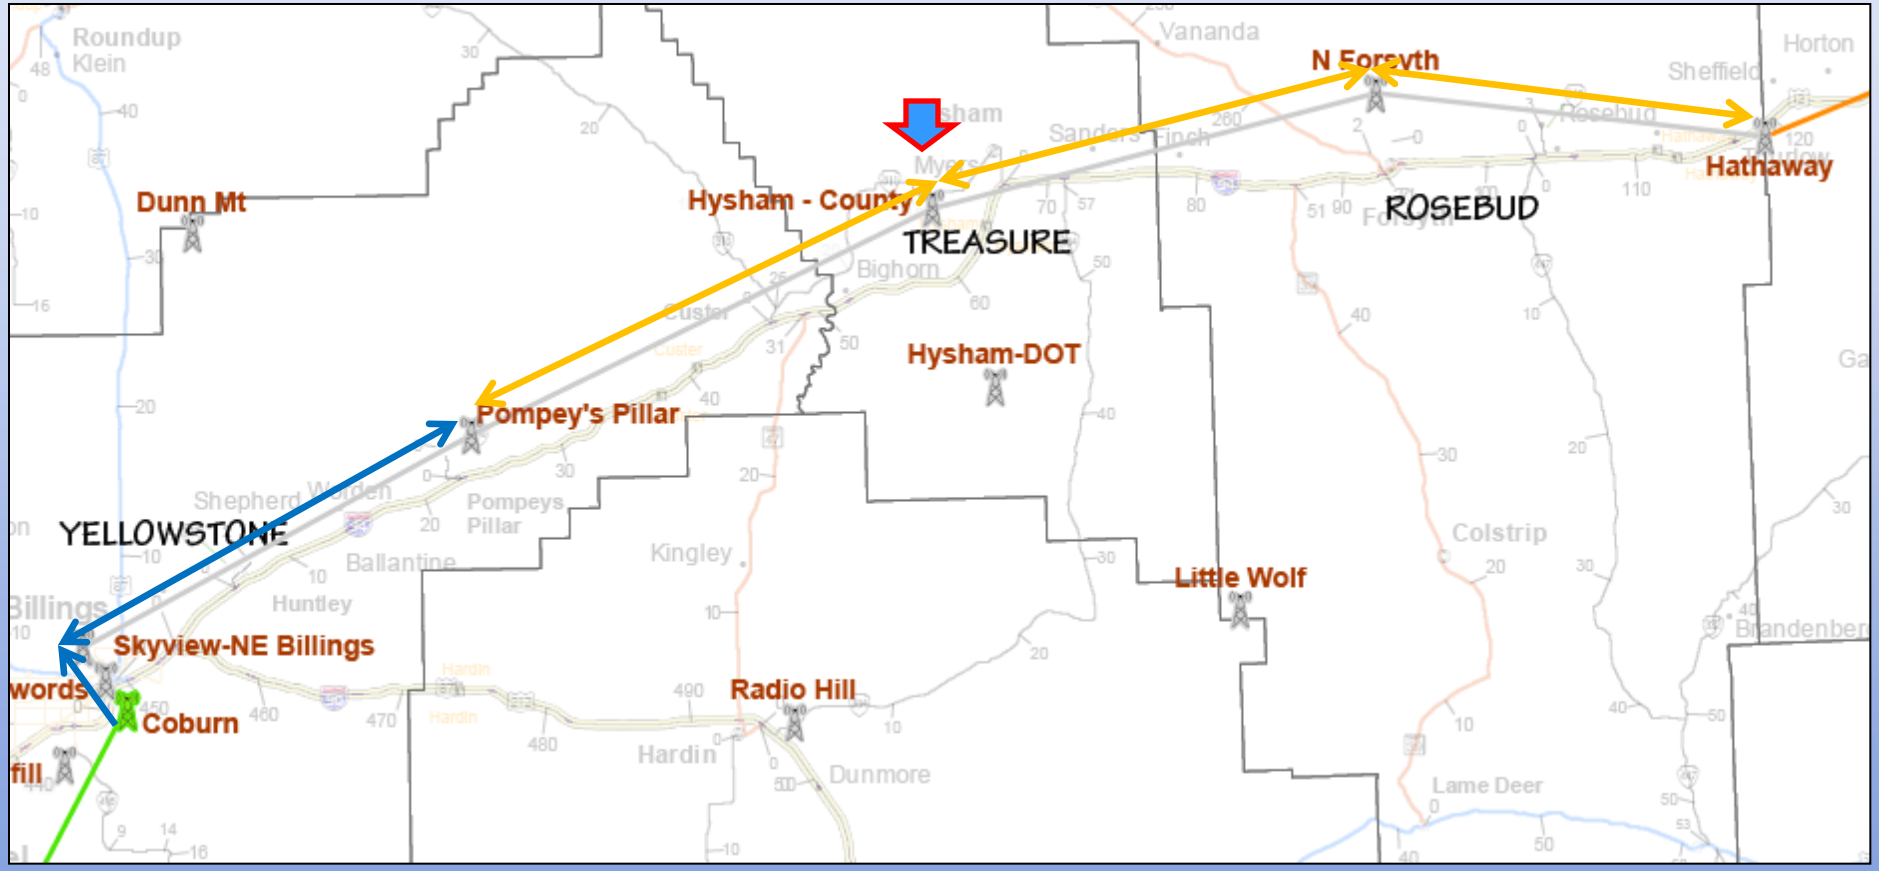

Border Interoperability Demonstration Grant

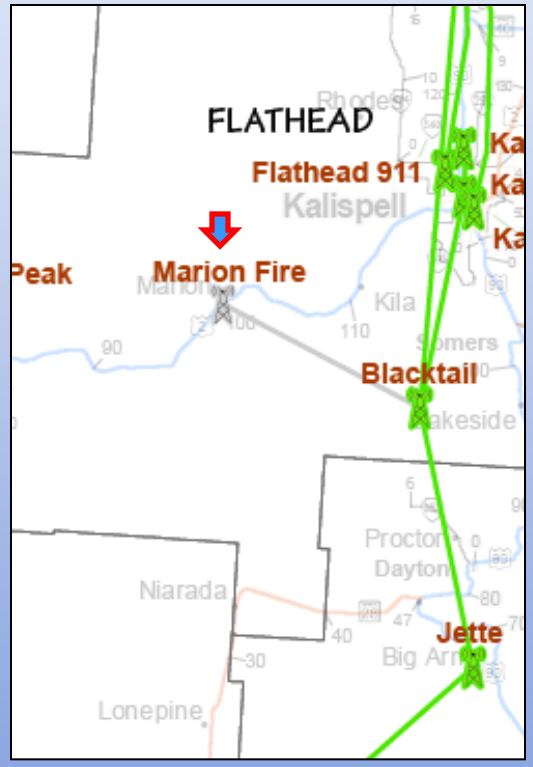

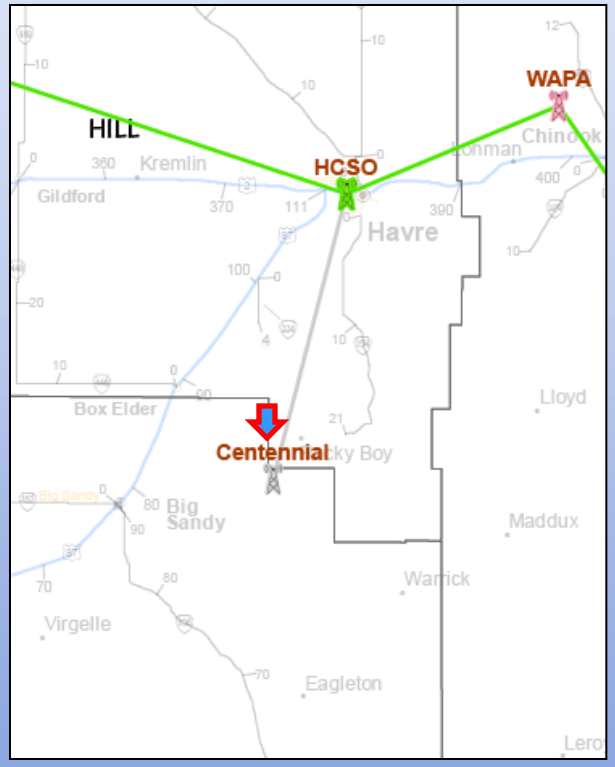

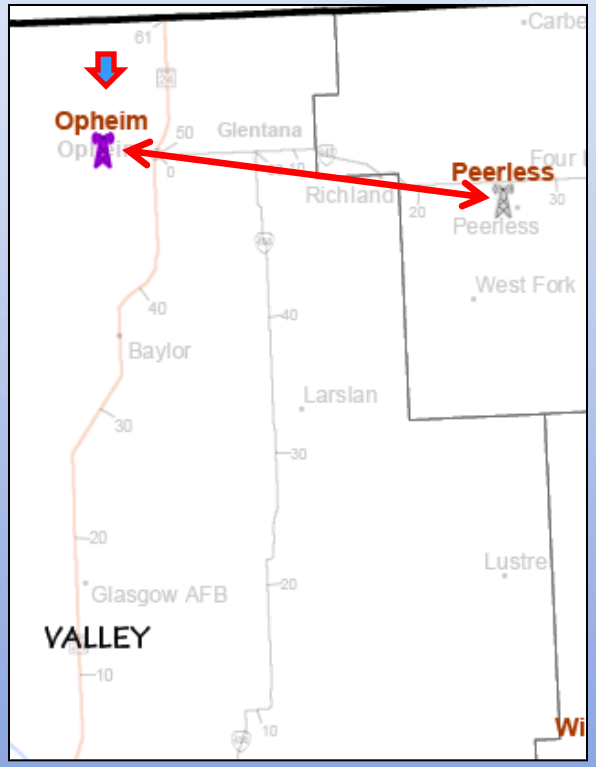

Trunked Coverage

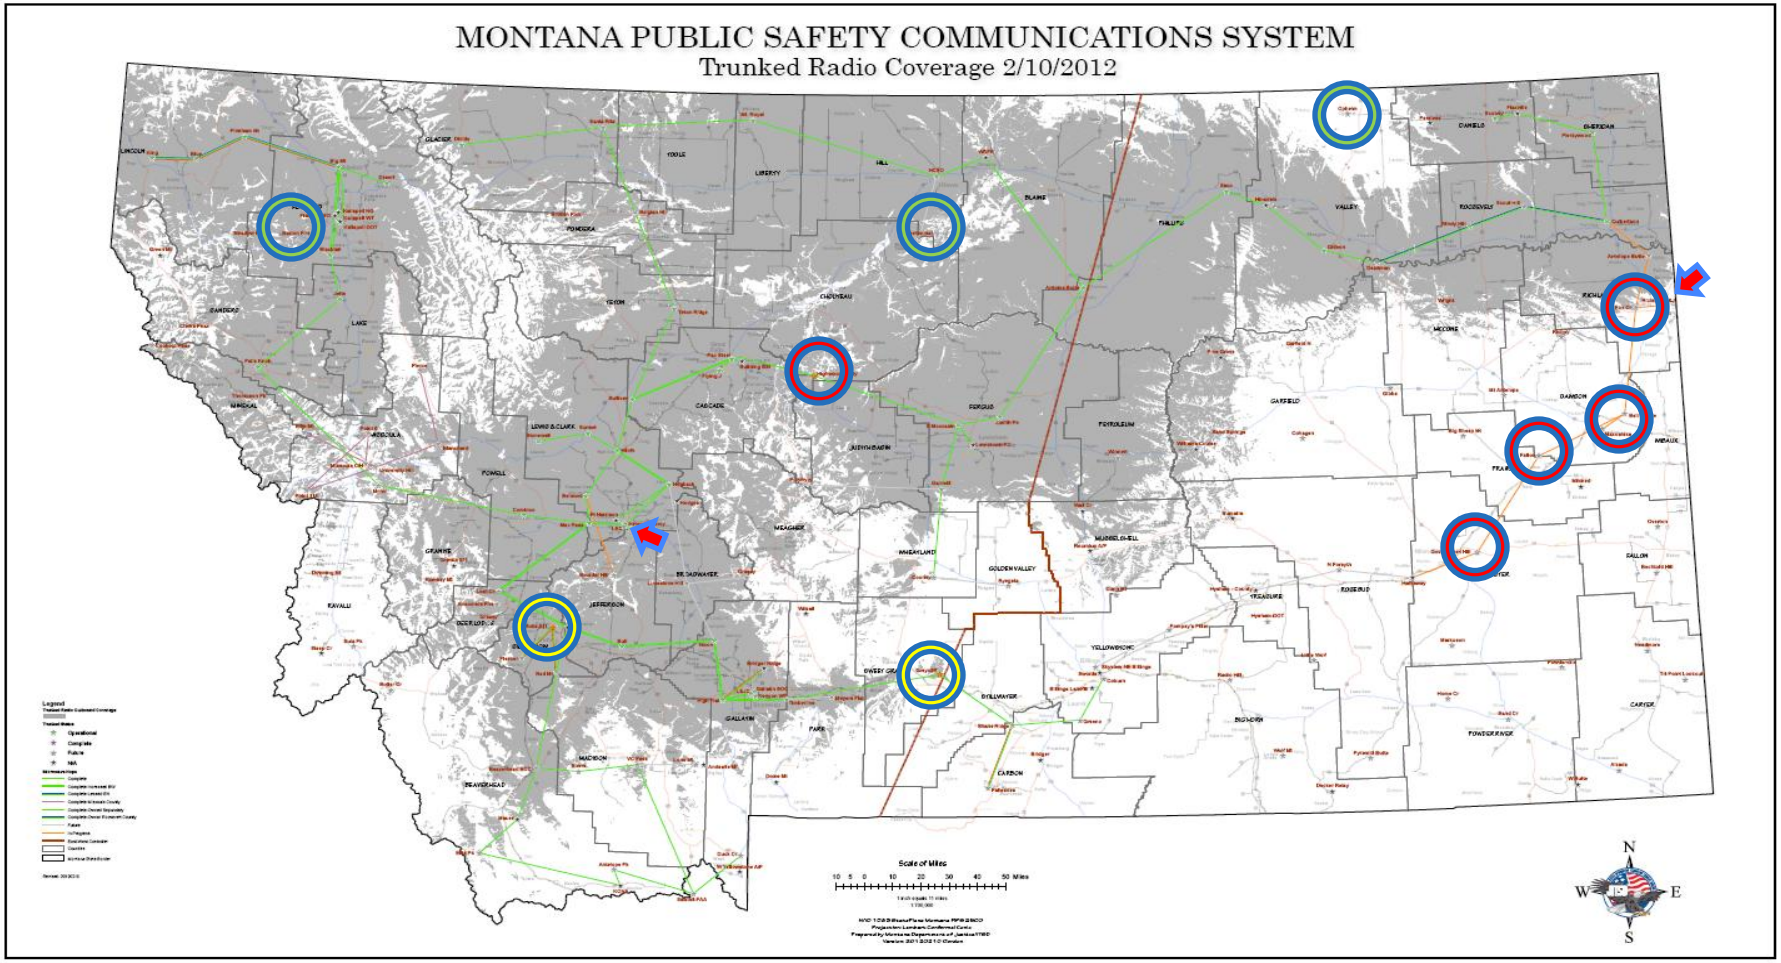

Trunked Radio Coverage

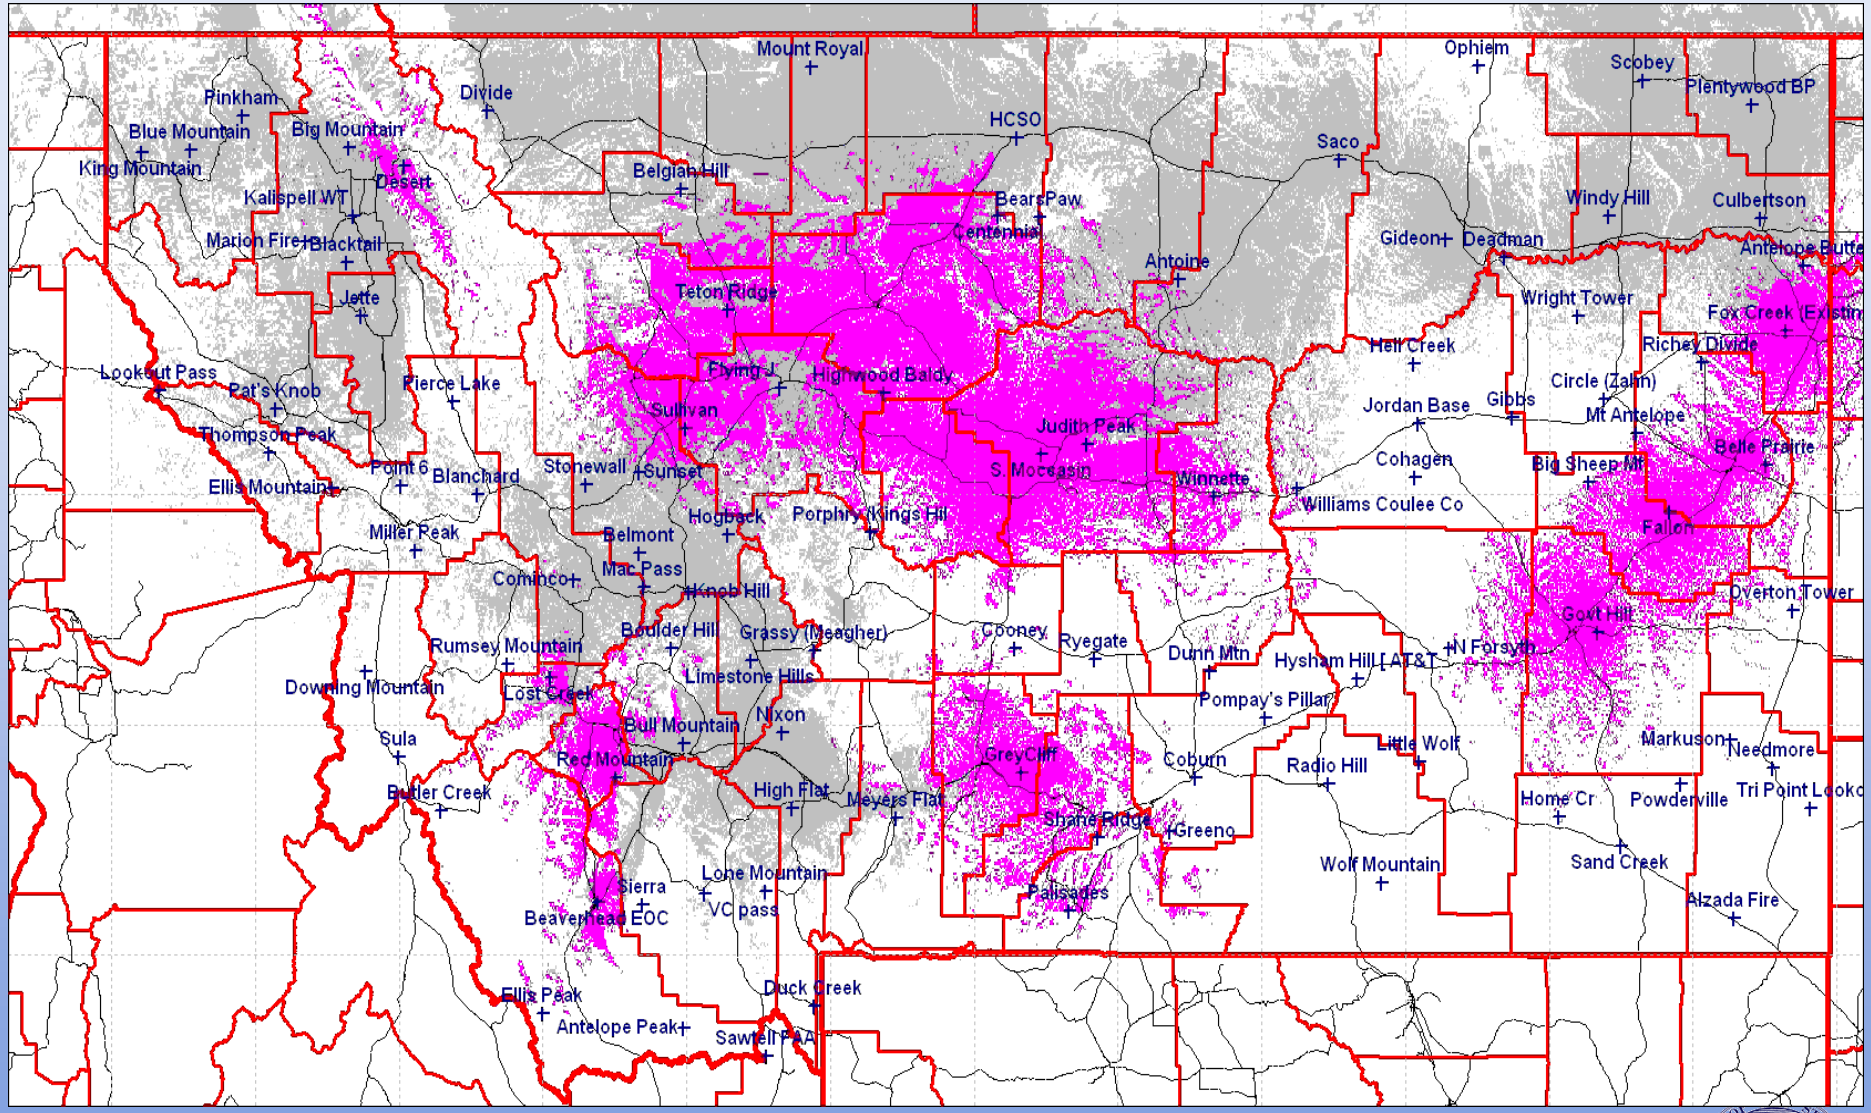

Montana Public Safety Communications Status Web Site

- Microwave Status: //apps.arcgis.com/hosted/Legend/chrome/index.html?appid=6d51939493d4490dbec4f63130967988&webmap=999952cfa867450f9b61a692ab4de9af
- Trunked Status: //apps.arcgis.com/hosted/Legend/chrome/index.html?appid=d0a58814a2af4bc7bf08b95d6fdb17d2&webmap=53b6a74bc23f4221a25ee055fb6f9829

Public Safety Communications Evolution

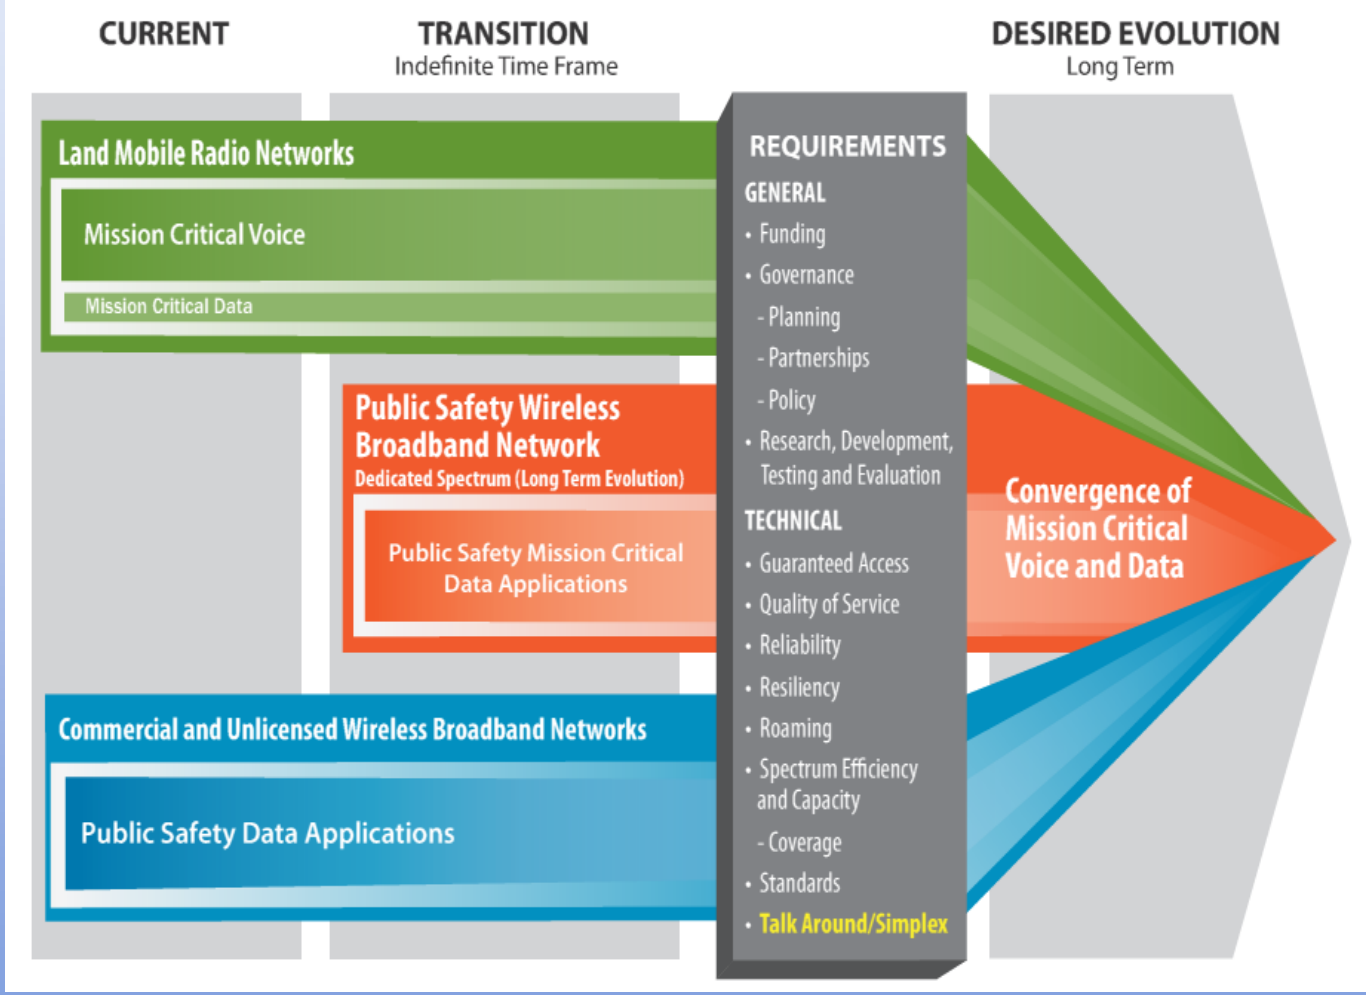

This conceptual framework outlines building wireless broadband data communications while maintaining LMR networks to support mission critical voice communications

Questions?
